


MUVATTUPUZHA VALLEY IRRIGATION PROJECT

LEFT BANK CANALS

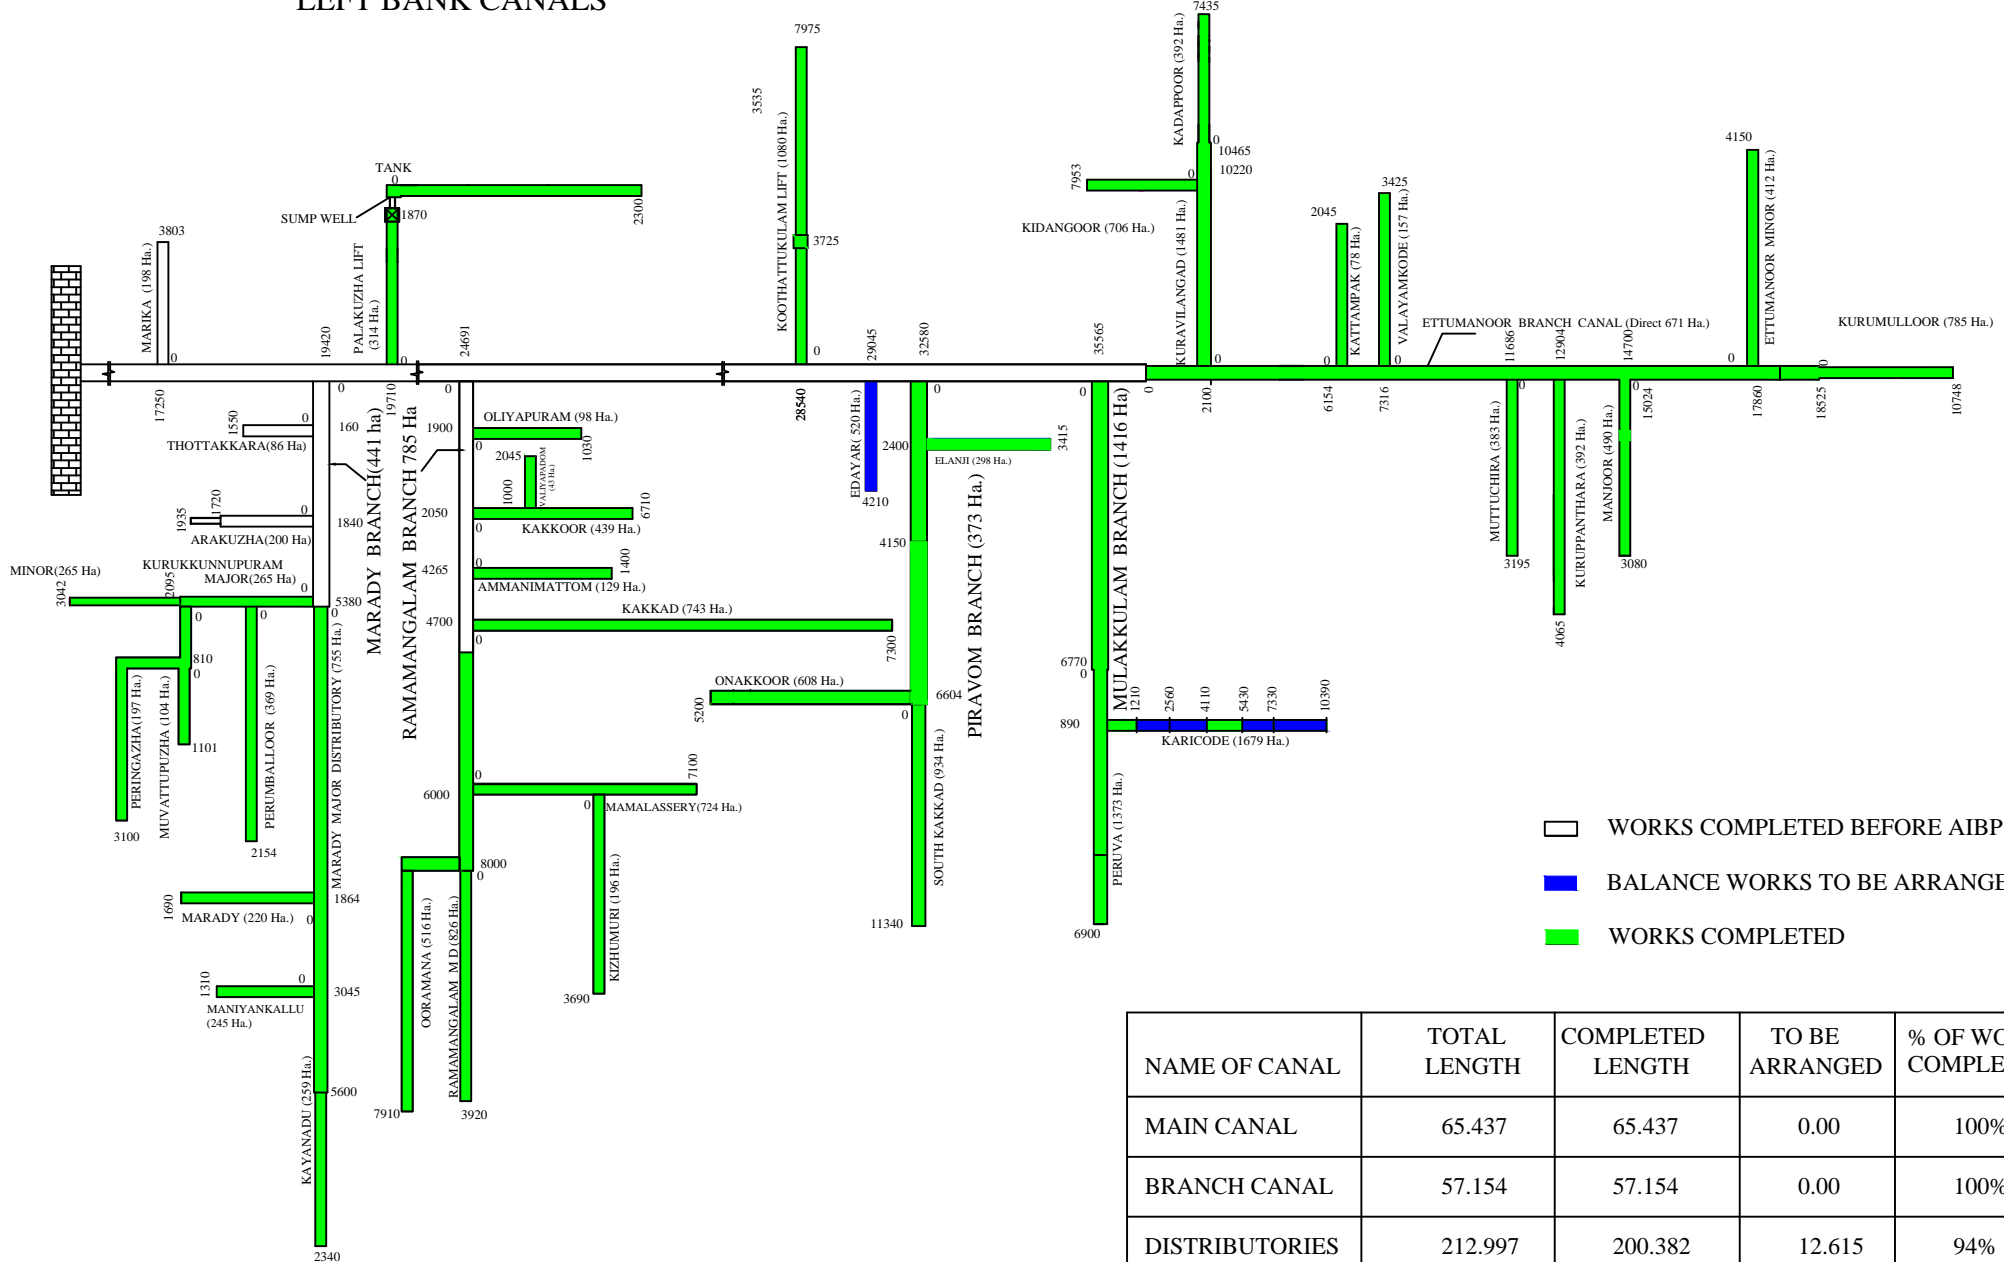

- WORKS COMPLETED BEFORE AIBP
- BALANCE WORKS TO BE ARRANGED
- WORKS COMPLETED

NAME OF CANAL	TOTAL LENGTH	COMPLETED LENGTH	TO BE ARRANGED	% OF WORK COMPLETED
MAIN CANAL	65.437	65.437	0.00	100%
BRANCH CANAL	57.154	57.154	0.00	100%
DISTRIBUTORIES	212.997	200.382	12.615	94%
TOTAL	335.588	322.973	12.615	96%
